



TEST BORING RECORD B1-1

PROJECT: GDOT MMIP SR 400 Express Lanes - PI# 0001757
CLIENT: AECOM/GDOT
PROJECT LOCATION: SR 400 - Fulton and Forsyth Counties
LOCATION: BFI 1 - Spalding Dr. over SR 400
DRILLER: S&ME CME-550X (SN 292103)
DRILLING METHOD: Hollow Stem Auger % ENERGY: 91.4
DEPTH TO - WATER> INITIAL: ∅ N/E AFTER 24 HOURS: ∅

PROJECT NO.: 2018089
LATITUDE: 33.95649946
LONGITUDE: -84.35704534
ELEVATION: 1038.6 feet
LOGGED BY: J. Cobkit
DATE: 2/28/2019
N/M CAVING> C

This information pertains only to this boring and should not be interpreted as being indicative of the site.

Depth (feet)	Elevation (ft-NAVD 88)	Description	Graphic	Groundwater	Sample Type	N-Value	Graphic Depiction													
							● BLOW COUNT	▲ NATURAL MOISTURE	PLASTIC LIMIT					LIQUID LIMIT						
									10	20	30	40	60	100	10	20	30	40	60	100
0																				
		ASPHALT: 9 inches																		
		GRADED AGGREGATE BASE: 2 inches																		
		FILL: Medium dense red silty medium to fine SAND, trace mica and rock fragments (SM)																		
1035																				
5																				

Auger only upper 6 ft.



TEST BORING RECORD B1-1

PROJECT: GDOT MMIP SR 400 Express Lanes - PI# 0001757
CLIENT: AECOM/GDOT
PROJECT LOCATION: SR 400 - Fulton and Forsyth Counties
LOCATION: BFI 1 - Spalding Dr. over SR 400
DRILLER: S&ME CME-550X (SN 292103)
DRILLING METHOD: Hollow Stem Auger % ENERGY: 91.4
DEPTH TO - WATER> INITIAL: ∅ N/E AFTER 24 HOURS: ∅

PROJECT NO.: 2018089
LATITUDE: 33.95649946
LONGITUDE: -84.35704534
ELEVATION: 1038.6 feet
LOGGED BY: J. Cobkit
DATE: 2/28/2019
N/M CAVING> C

This information pertains only to this boring and should not be interpreted as being indicative of the site.

Depth (feet)	Elevation (ft-NAVD 88)	Description	Graphic	Groundwater	Sample Type	N-value	Graphic Depiction									
							● BLOW COUNT ▲ NATURAL MOISTURE PLASTIC LIMIT LIQUID LIMIT 10 20 30 40 60 100									
		Medium dense white brown silty medium to fine SAND, trace mica (SM)				9										
40	1000	Loose gray white silty coarse to fine SAND (SM)														
		Auger Refusal at 42.5 ft.														
45	995															
	990															
50																
	985															
55																
	980															
60																
	975															
65																
	970															
70																

Auger only upper 6 ft.




TEST BORING RECORD B1-2

PROJECT: GDOT MMIP SR 400 Express Lanes - PI# 0001757
CLIENT: AECOM/GDOT
PROJECT LOCATION: SR 400 - Fulton and Forsyth Counties
LOCATION: BFI 1 - Spalding Dr. over SR 400
DRILLER: S&ME CME-550X (SN 292103)
DRILLING METHOD: Hollow Stem Auger % ENERGY: 91.4
DEPTH TO - WATER> INITIAL: ∅ N/E AFTER 24 HOURS: ∅

PROJECT NO.: 2018089
LATITUDE: 33.95708066
LONGITUDE: -84.35547412
ELEVATION: 1032.6 feet
LOGGED BY: J. Cobkit
DATE: 2/28/2019
N/M CAVING> C

This information pertains only to this boring and should not be interpreted as being indicative of the site.

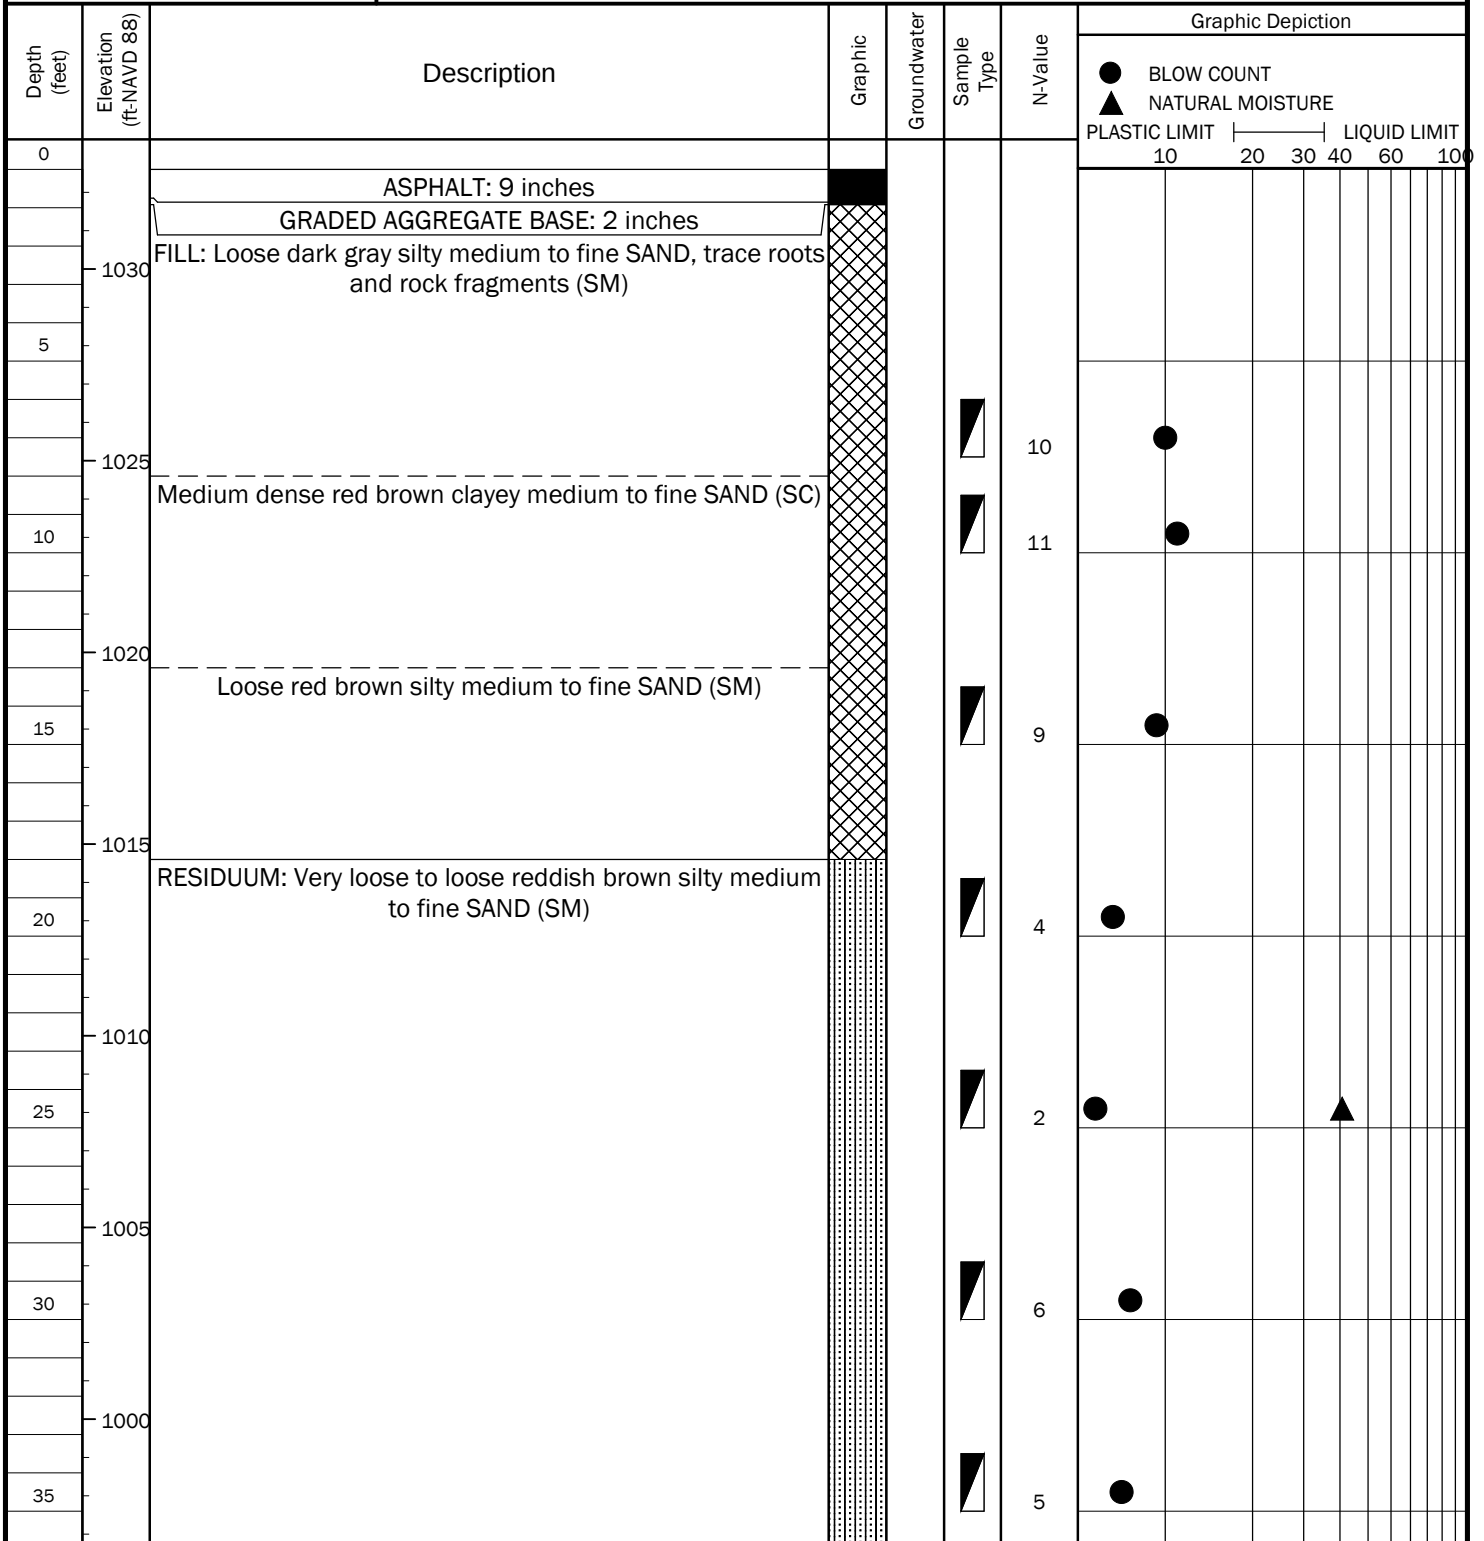

Auger only upper 6 ft.



DEPTH TO - WATER> INITIAL: N/E AFTER 24 HOURS:

N/M CAVING> C _____

[illegible]

Page 2 of 2

This information pertains only to this boring and should not be interpreted as being indicative of the site.



TEST BORING RECORD B2-1

PROJECT: GDOT MMIP SR 400 Express Lanes - PI# 0001757
CLIENT: AECOM/GDOT
PROJECT LOCATION: SR 400 - Fulton and Forsyth Counties
LOCATION: BFI 2 - Roberts Drive over SR 400
DRILLER: S&ME CME-550X (SN 292103)
DRILLING METHOD: Hollow Stem Auger % ENERGY: 91.4
DEPTH TO - WATER> INITIAL: ∅ N/E AFTER 24 HOURS: ∅

PROJECT NO.: 2018089
LATITUDE: 33.99145926
LONGITUDE: -84.33860112
ELEVATION: 1050.2 feet
LOGGED BY: J. Cobkit
DATE: 2/8/2019
N/M CAVING> C

This information pertains only to this boring and should not be interpreted as being indicative of the site.

Depth (feet)	Elevation (ft-NAVD 88)	Description	Graphic	Groundwater	Sample Type	N-value	Graphic Depiction									
							● BLOW COUNT ▲ NATURAL MOISTURE PLASTIC LIMIT LIQUID LIMIT 10 20 30 40 60 100									
0	1050	TOPSOIL: 2 inches RESIDUUM: White tan silty medium to fine SAND (SM)														
5	1045	PARTIALLY WEATHERED ROCK: Sampled as very dense white tan silty medium to fine SAND				100/ 10"										
10	1040	RESIDUUM: Medium dense brown micaceous silty coarse to fine SAND (SM)				14										
15	1035	Medium dense brown micaceous silty medium to fine SAND (SM)				15										
20	1030	PARTIALLY WEATHERED ROCK: Sampled as very dense white red gray silty coarse SAND Auger Refusal at 18.7 ft.				100/2"										
25	1025															
30	1020															
35	1015															

Boring was offset 3 times, the first 3 borings all refused at 6 feet.
Auger only upper 6 ft.



TEST BORING RECORD B2-2

PROJECT: GDOT MMIP SR 400 Express Lanes - PI# 0001757
CLIENT: AECOM/GDOT
PROJECT LOCATION: SR 400 - Fulton and Forsyth Counties
LOCATION: BFI 2 - Roberts Drive over SR 400
DRILLER: S&ME Diedrich D-50 Track (SN 382)
DRILLING METHOD: Hollow Stem Auger % ENERGY: 98.1
DEPTH TO - WATER> INITIAL: ∅ N/E AFTER 24 HOURS: ∅ N/M CAVING> C

PROJECT NO.: 2018089
LATITUDE: 33.99158441
LONGITUDE: -84.33817267
ELEVATION: 1034.4 feet
LOGGED BY: J. Cobkit
DATE: 5/20/2019

This information pertains only to this boring and should not be interpreted as being indicative of the site.

Depth (feet)	Elevation (ft-NAVD 88)	Description	Graphic	Groundwater	Sample Type	N-Value	Graphic Depiction													
							● BLOW COUNT	▲ NATURAL MOISTURE	PLASTIC LIMIT LIQUID LIMIT											
0							10	20	30	40	60	100								
		CONCRETE: 9.25 inches																		
		GRADED AGGREGATE BASE: 6 inches																		
		FILL: Medium dense brown white gray black micaceous silty medium to fine SAND with rock fragments (SM)				24		▲		●										
5	1030	PARTIALLY WEATHERED ROCK: Sampled as very dense brown silty medium to fine SAND, trace mica and rock fragments				100/6"														●
		Auger Refusal at 4.1 ft.																		
10	1025																			
15	1020																			
20	1015																			
25	1010																			
30	1005																			
35	1000																			
